



	<b>(B)</b>	Name	Duration	Start	Finish	Predecessors	Resource Names	19 S S M
1	Ö	Project Management a	11 days?	04/03/24 08:00	18/03/24 17:00			
2	Ö	Communication Plan	2 days	04/03/24 08:00	05/03/24 17:00		Halil Kasapoglu	
3	Ö	Gant chart Initialization	3 days	14/03/24 08:00	18/03/24 17:00	2	Irem Nur Yildirim	
	Ö	Requirement preparation	2 days	15/03/24 08:00	18/03/24 17:00	2;6	Rukiye Aslan ;Halil Kasapogl	
,	Ö	RAM initialization	2 days	11/03/24 08:00	12/03/24 17:00	2	Yasin Bastug	
	Ö	Glossary	2 days?	11/03/24 08:00	12/03/24 17:00	2	Rukiye Aslan ;Halil Kasapogl	
	Ö	Design	20.5 days?	19/03/24 08:00	16/04/24 13:00	73		
	O	Main page	12 days?	19/03/24 10:00	04/04/24 10:00			
	O	User login	5 days?	19/03/24 08:00	25/03/24 17:00			
	O	Admin Login	2 days?	23/03/24 08:00	26/03/24 17:00			
	O	User Page	15 days?	23/03/24 08:00	12/04/24 17:00			
	Ö	Director Pages	8 days?	25/03/24 08:00	03/04/24 17:00			
	O	Actor/Actrice Pages	8 days?	25/03/24 08:00	03/04/24 17:00			
		User feed page	20 days?	19/03/24 12:00	16/04/24 13:00			
	<b>₽</b>	Research and Analysis	2.5 days	14/03/24 08:00	18/03/24 13:00		Yasin Bastug;Rukiye Asl	
		Git version control resea	2.5 days	14/03/24 08:00	18/03/24 13:00		Erkam Gokcepinar;Irem Nur	
		Wiki	1.5 days	14/03/24 08:00	15/03/24 13:00		Furkan Senkal;Irem Nur Yildirir	n
		Wikidata and API	1.5 days	14/03/24 08:00	15/03/24 13:00		Irem Nur Yildirim;Halil Kasap	
		SPARQL	1 day	14/03/24 08:00	14/03/24 17:00		Rukiye Aslan ;Bugra ;Yasin	
		System Modeling	11 days?	15/04/24 10:00	30/04/24 10:00			
		Use Case Diagram	11 days?	15/04/24 10:00	30/04/24 10:00		Irem Nur Yildirim;Furkan Sen	
		Class Diagram	11 days?	15/04/24 10:00	30/04/24 10:00		Erkam Gokcepinar;Halil Kasa	
	O	Sequence Diagram	11 days?	15/04/24 10:00	30/04/24 10:00		Rukiye Aslan ;Yasin Bastug;	
		Development	56.625 day	20/02/24 11:00	08/05/24 17:00			
	<b>★!</b>	Android	56.625 day	20/02/24 11:00	08/05/24 17:00		Furkan Senkal; Erkam Go	
		Backend	50.625 day	20/02/24 11:00	30/04/24 17:00			
	O	Database setup	16 days?	01/04/24 08:00	22/04/24 17:00		Rukiye Aslan	
	Ö	Docker setup	1 day?	23/04/24 08:00	23/04/24 17:00	27	Irem Nur Yildirim	
	•	API connection	2 days	29/04/24 08:00	30/04/24 17:00	32	Halil Kasapoglu	
		Login Pages	1 day?	20/02/24 11:00	21/02/24 11:00			
		API	20 days?	01/04/24 08:00	26/04/24 17:00			
	•	API initialization	20 days?	01/04/24 08:00	26/04/24 17:00		Irem Nur Yildirim	
,	Ö	Frontend	12 days?	23/04/24 08:00	08/05/24 17:00			
ļ.	O	Main page	2 days?	27/04/24 08:00	30/04/24 17:00		Erkam Gokcepinar;Furkan S	

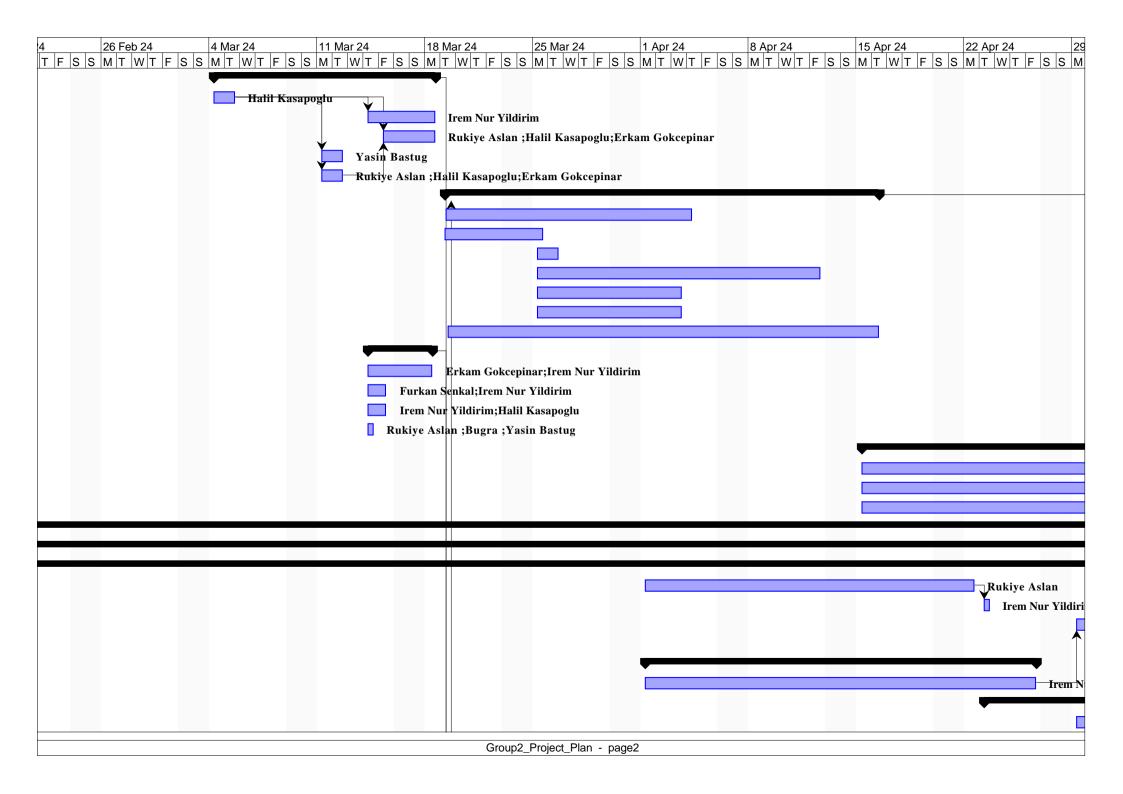

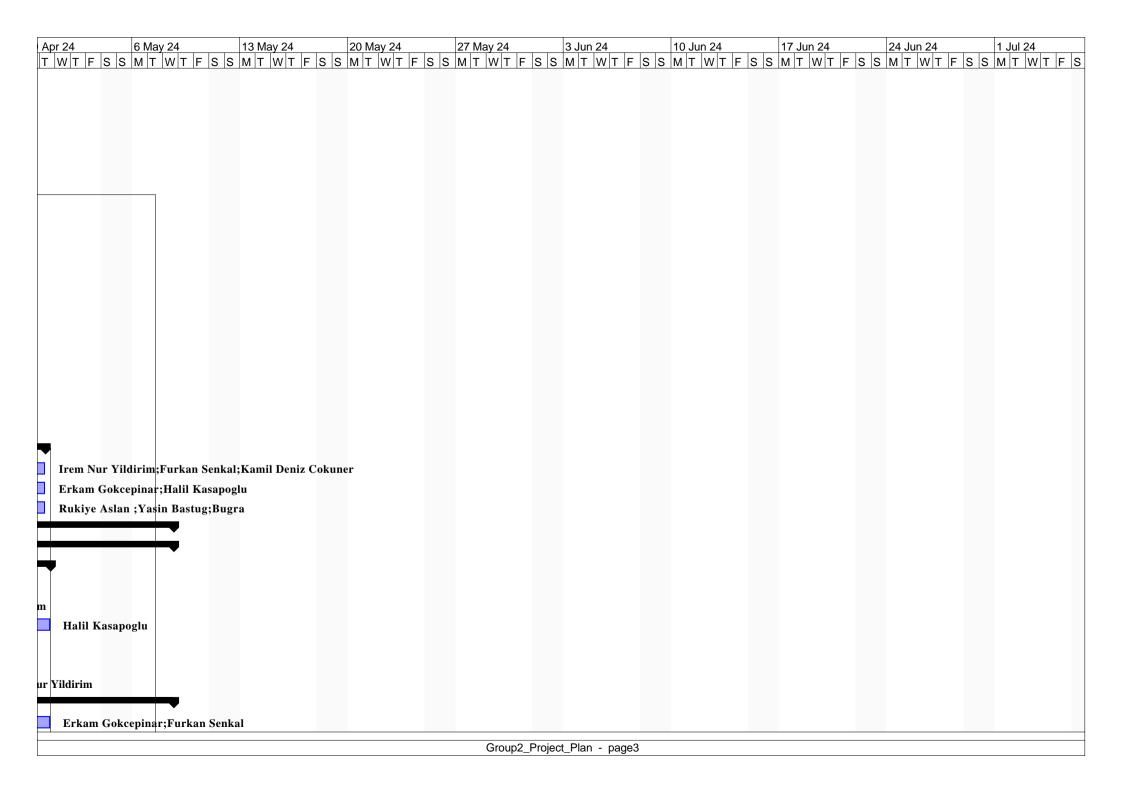

	<b>(((((((((((((</b>	Name	Duration	Start	Finish	Predecessors	Resource Names S	19 S M
35		User page	5 days?	27/04/24 08:00	03/05/24 17:00		Furkan Senkal	
36		Director Page	7 days?	27/04/24 08:00	07/05/24 17:00		Erkam Gokcepinar	
37		Actor Page	7 days?	25/04/24 08:00	03/05/24 17:00		Erkam Gokcepinar	
8		User feed	4 days?	27/04/24 08:00	02/05/24 17:00		Furkan Senkal	
9		Login pages	8 days?	23/04/24 08:00	02/05/24 17:00		Erkam Gokcepinar;Furkan S	
0		Review after design	1.5 days?	07/05/24 13:00	08/05/24 17:00	7	Furkan Senkal;Erkam Gokce	
1		Web	9.625 days?	25/04/24 11:00	08/05/24 17:00			
12	<b>∰ </b> ★!	Backend	9.625 days?	25/04/24 11:00	08/05/24 17:00		Irem Nur Yildirim;Rukiye	
3		Login endpoint	0.312 days?	25/04/24 11:00	25/04/24 14:30		Rukiye Aslan ;Halil Kasapoglu	
4		Register endpoint	0.625 days?	25/04/24 11:00	25/04/24 17:00		Irem Nur Yildirim	
5		Recently released fil	0.625 days	26/04/24 11:00	26/04/24 17:00		Rukiye Aslan	
6		Users endpoints	3.5 days?	27/04/24 11:00	02/05/24 13:00		Halil Kasapoglu;Irem Nur Yild	
7		Film endpoints	3.812 days?	26/04/24 11:00	02/05/24 09:30		Irem Nur Yildirim;Rukiye Aslan	
18		Wikidata guery endp	2.625 days?	29/04/24 11:00	01/05/24 17:00		Halil Kasapoglu	
9		Email verification end	3.625 days?	30/04/24 11:00	03/05/24 17:00		Irem Nur Yildirim	
0		Log out endpoint	4.625 days?	02/05/24 11:00	08/05/24 17:00		Rukiye Aslan	
51		API	0.625 days?	25/04/24 11:00	25/04/24 17:00			
52		API initialization	0.625 days?	25/04/24 11:00	25/04/24 17:00			
53	<b>∰ </b> ★!	Frontend	8.625 days?	25/04/24 11:00	07/05/24 17:00		Bugra ;Kamil Deniz Cok	
54		Login page	0.625 days	25/04/24 11:00	25/04/24 17:00		Yasin Bastug	
55		Register page	0.625 days	26/04/24 11:00	26/04/24 17:00		Kamil Deniz Cokuner	
56		Forgot Password page	0.625 days?	26/04/24 11:00	26/04/24 17:00		Bugra	
57		Search Bar	1 day?	29/04/24 11:00	30/04/24 11:00		Yasin Bastug	
58		Main page	0.312 days?	29/04/24 11:00	29/04/24 14:30		Yasin Bastug;Kamil Deniz Co	
59		Profile page	4.625 days?	01/05/24 11:00	07/05/24 17:00		Bugra	
60		Film list page	4.625 days?	01/05/24 11:00	07/05/24 17:00		Kamil Deniz Cokuner	
61		Actor page	4.625 days?	01/05/24 11:00	07/05/24 17:00		Yasin Bastug	
62		Director page	4.625 days?	01/05/24 11:00	07/05/24 17:00		Bugra	
63		Verification pages	4.625 days?	01/05/24 11:00	07/05/24 17:00		Kamil Deniz Cokuner	
64		Customers	3 days?	23/02/24 11:00	28/02/24 11:00	70		
65		User scenario #1	3 days?	23/02/24 11:00	28/02/24 11:00			
66		User scenario #2	3 days?	23/02/24 11:00	28/02/24 11:00		Irem Nur Yildirim	
67		User scenario #3	3 days?	23/02/24 11:00	28/02/24 11:00		Irem Nur Yildirim	
68		User scenario #4	3 days?	23/02/24 11:00	28/02/24 11:00		Irem Nur Yildirim	

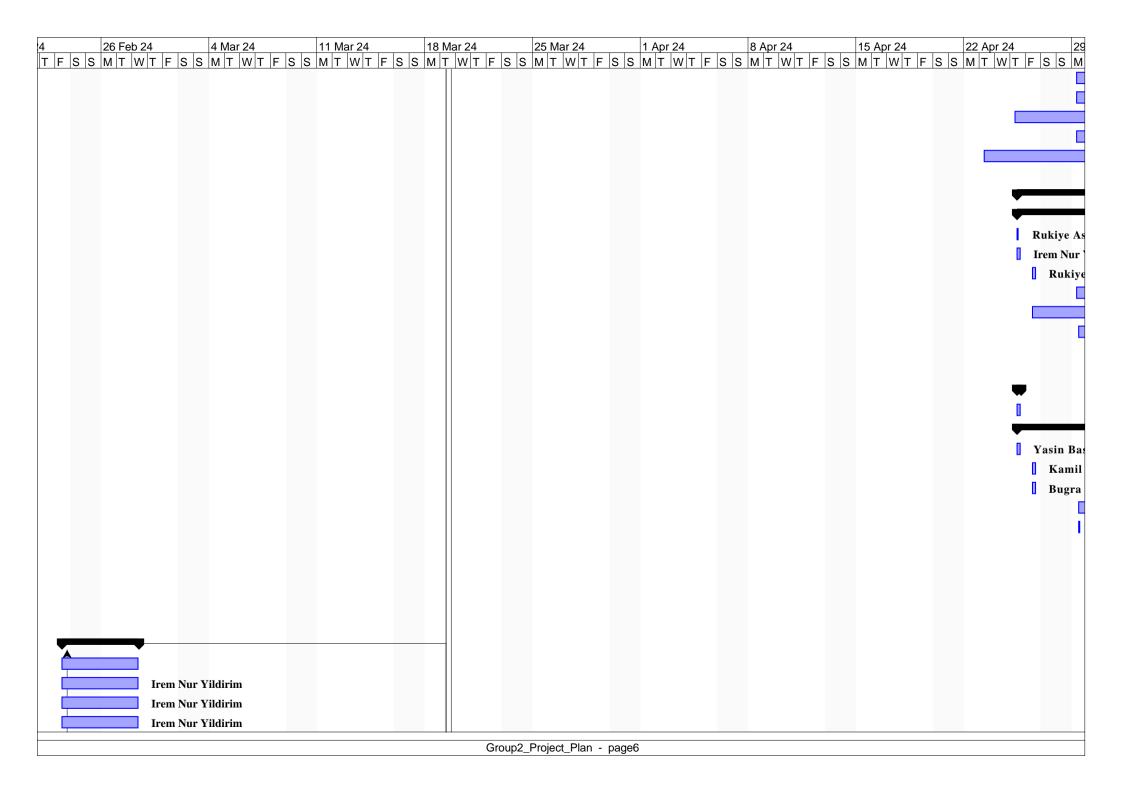

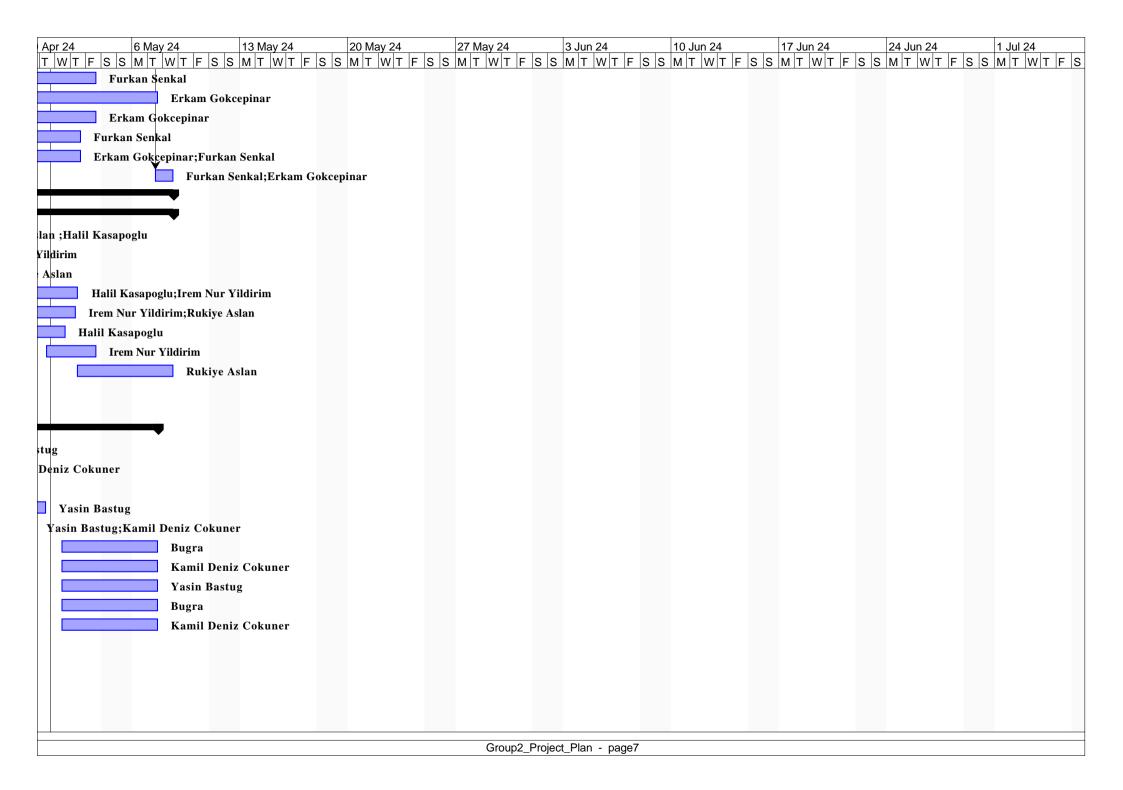

	<b>®</b>	Name	Duration	Start	Finish	Predecessors	Resource Names S	1 S S N
69		User scenario #5	3 days?	23/02/24 11:00	28/02/24 11:00		Irem Nur Yildirim	
70	<b>★!</b>	Decisions and Revisions	3 days	20/02/24 11:00	23/02/24 11:00		Yasin Bastug;Rukiye Asl	
71		Discuss project domain	3 days	20/02/24 11:00	23/02/24 11:00		Rukiye Aslan ;Halil Kasapogl	
72		Discuss project frame an	2 days	20/02/24 11:00	22/02/24 11:00		Furkan Senkal; Erkam Gokce	
73		Milestone #1	0 days	19/03/24 10:00	19/03/24 10:00	1;15;64		
74		Milestone #2	0 days	30/04/24 10:00	30/04/24 10:00	20		
75		Milestone #3	0 days	17/05/24 10:00	17/05/24 10:00			
76	•	Deployment	6 days	30/05/24 11:00	07/06/24 11:00			

